Michigan Department of Natural Resources

Forest Resources Division

FOREST TREATMENT PROPOSAL

Location: Grayling FMU						Proposal: **C72-935**
County: Crawford	T27N	R1W	Sec. 36 N1/2NW, SWNE	YOE: 2018	Comp: 284	Stands: 14, 20

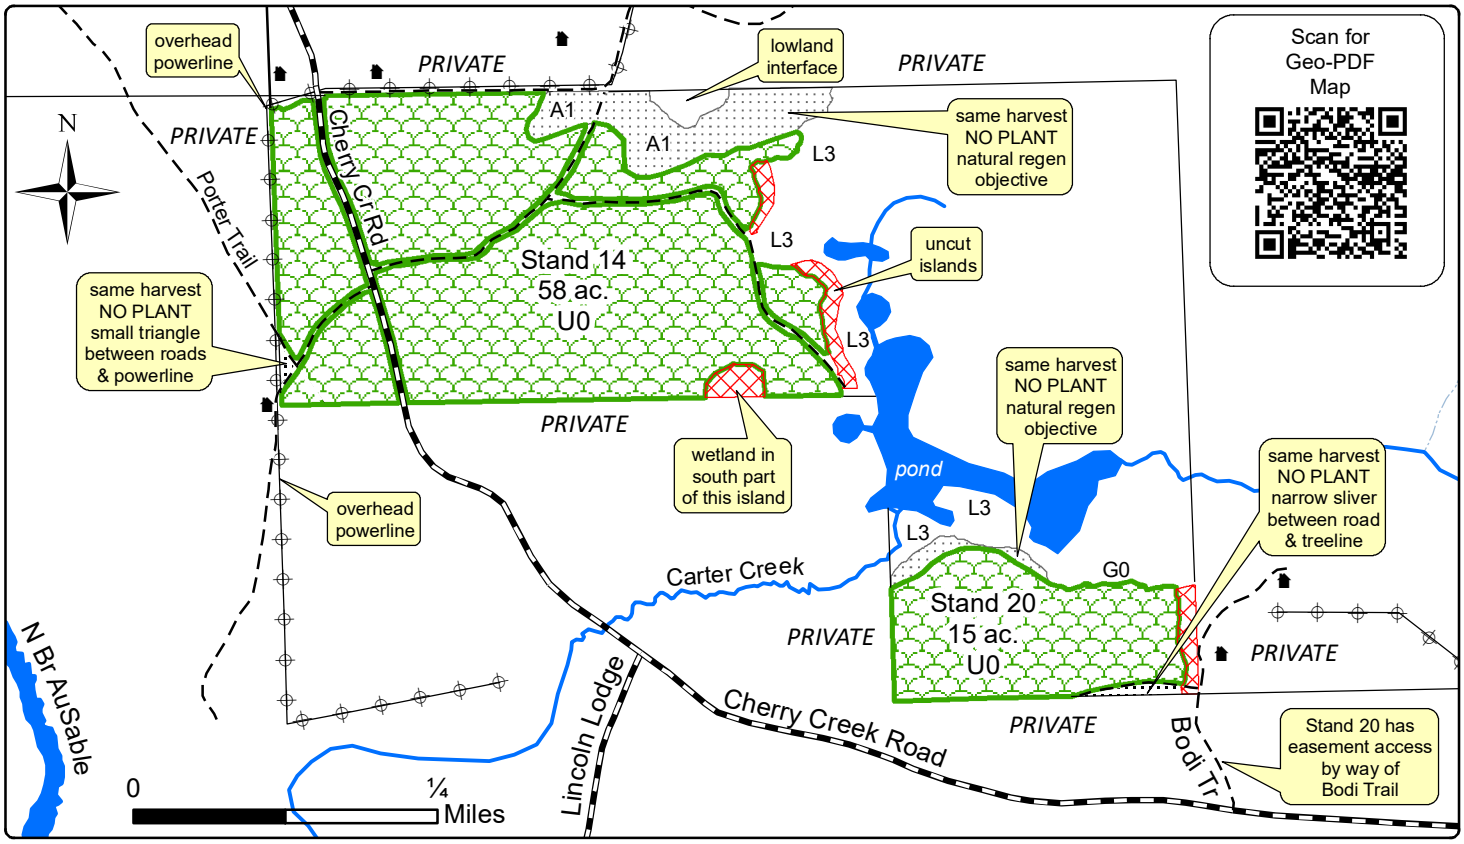

PROOFING COMMENTS
Rec: None
Water: streams, ponds, wetlands within 500 ft
HAL: None known at this time
MNFI: KW recorded in the past in managed habitat to the NW
Reviewed & edited: Feb 3, 2023 JC

ACTIVITY TRACKING	

Covertype Objective: Planted Red Pine	Acres: **73**
Approved Methods: Trench & plant RP at standard spacing. Additional treatments may include roller chopping & herbicide. Leave open existing roads within the planting area.	
Timbersale number: 72-042-19	
Sale admin staff: Ewald	
Harvesting completed by: Dec 2022	
Contract TCR date: 01/12/2023	

Comments:

Stands 14 & 20 were initially cut in spring of 2022 except for a tree-length buffer along the perimeter. The loggers then moved back in and cut the buffers in the last quarter of 2022. Stumps were cut low and the sale was chipped. The amount of riparian interface varies with the level of beaver activity on Carter Creek and its associated ponds; any needed set-backs from water features will be flagged-in before trenching begins.
