Michigan Department of Natural Resources
Forest Resources Division

FOREST TREATMENT PROPOSAL

Location: **Pigeon River Country**					Proposal: **C53-533**
County: Otsego	T31N	R01W	Sec. 1: SENE, N1/2SE	YOE: 2023	Comp: 49	Stands: 41

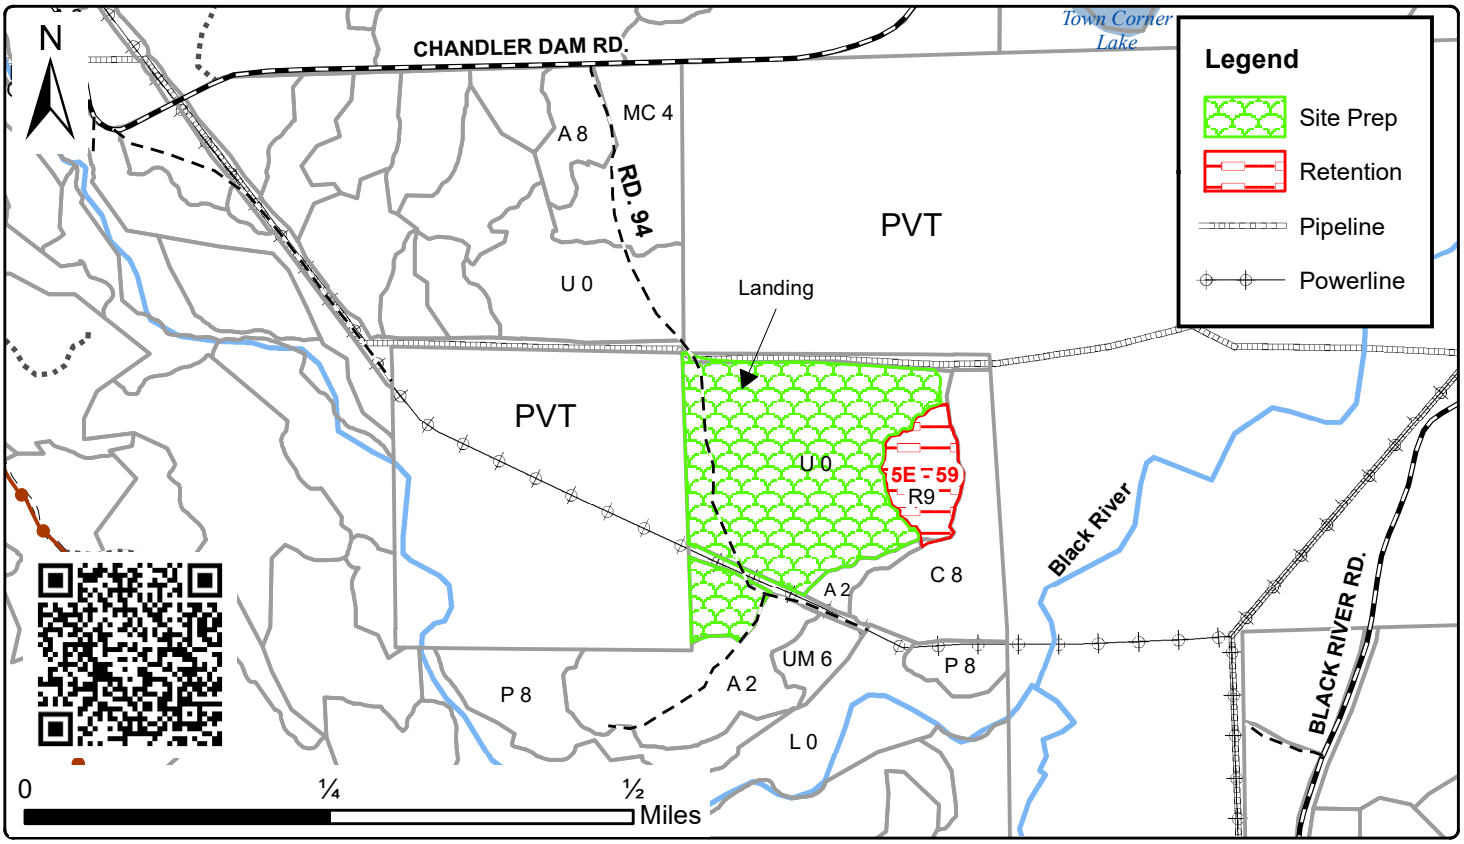

PROOFING COMMENTS
Rec: None
Water: Black River nearby
HAL: No occurrences within this area.
MNFI: No ocurrences.
Reviewed: *10/03/2023 GR*

ACTIVITY TRACKING	

Covertype Objective: **Planted red pine**	Acres: **21.5**
Approved Methods: Trench and plant to red pine. No herbicide needed. No oak wilt concerns. Pre-commercial thinning of cherry likely needed in year 3 or 4.	
Timbersale number: 53-013-22-01	
Sale admin staff: Greg Rekowski	
Harvesting completed by: Summer/fall 2022 - Biewer	
Contract TCR date:	

Comments:

Access via Road 94 off of Chandler Dam Road. Use the landing at the NW corner to stage equipment. Terrain is flat. A few areas of heavy cherry competition in the north half, trench through these areas if possible. The north edge is bounded by a pipeline and ROW. A powerline ROW and overhead lines cut through the southern end of the treatment. The west edge of the treatment borders private and is marked with blue paint. The southeast boundary will stop near young regenerating aspen on a slight ridge. TRENCH ALL THE WAY TO THE EDGES DUE TO SPARSE TREE COVER AND MINIMAL SHADING IMPACTS.
